Do not approve eight hires.

A targeted response fixes the real constraints and uses spare capacity before expanding payroll.

RECOMMENDED OPERATING PLAN

TRANSFER

2 agents

H02 Lakeview -> H01 Greenfield

HIRE

2 Fixed

H04 Hillcrest

INTERVENE

H03

Fund the hold-reduction programme

FIRST-MONTH SPEND

BDT 62,800

BUDGET RESERVE

BDT 7,200

WHY THIS IS BETTER

Use idle capacity

H02 is at 56.17% Week 2 utilisation and can release two Fixed agents within Cluster A.

Hire only at the hard gap

H04 is the most constrained hub at 95.87% utilisation; two hires close its forecast gap.

Fix the process at H03

64.42% of Riverside Week 2 holds are agent-side. Hiring alone would not remove Late Dispatch.

Decision: approve the targeted plan, not the eight-agent request. Accept a managed two-week Riverside exception to the 85% planning target while keeping projected workload below the 40-attempt standard.

Demand rose faster than staffing capacity.

Across the two-week observation window, both orders and delivery attempts accelerated in Week 2.

ORDER GROWTH

+16.3%

10,534 -> 12,255 orders

ATTEMPT GROWTH

+19.0%

11,689 -> 13,906 attempts

ORDERS OBSERVED

22,789


13-26 October 2026

ATTEMPT PRESSURE

25,595

1.12 attempts per order overall

WEEKLY VOLUME COMPARISON

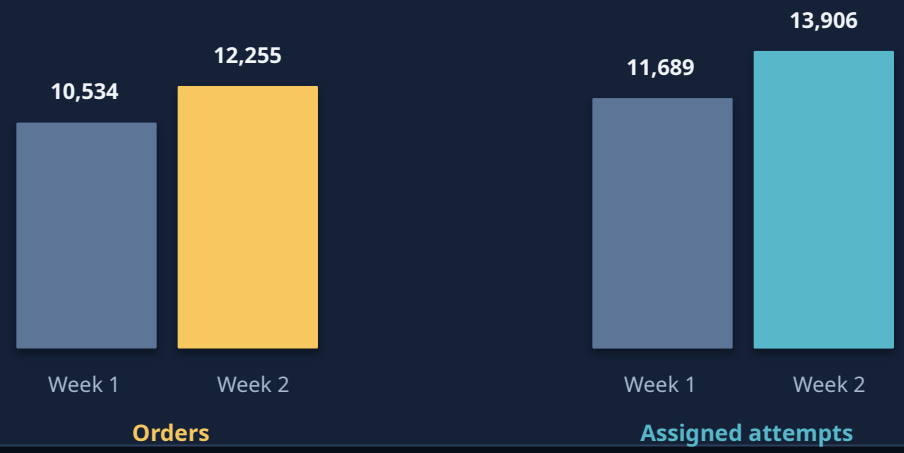

WHAT THE CHANGE MEANS

Attempts grew 2.6 percentage points faster than orders.

More volume is being generated by repeat work, not just more new parcels. Staffing should therefore use attempts per order, not order count alone.

Planning implication: forecast each hub's order volume using its observed 14-day attempts-per-order ratio, then apply the 85% workload target.

Capacity is uneven across the six hubs.

Week 2 utilisation is calculated as assigned attempts / (active agents x 40 attempts/day x 7 days).

WEEK 2 UTILISATION BY HUB



ACTION FLAGS

H04 Hillcrest 95.87%
Hire 2 Fixed agents

H03 Riverside 90.80%
Reduce agent-side holds

H01 Greenfield 88.64%
Receive 2 H02 transfers

H06 Westwood 80.36%
Monitor only

H05 Brookside 71.49%
Retain surplus; review returns

H02 Lakeview 56.17%
Eligible same-cluster donor

Riverside is a process problem; Brookside is a returns problem.

The interventions should be different. A blanket headcount response would miss both signals.

WEEK 2 HOLDS · H03

874

563 agent-side

AGENT-SIDE SHARE · H03

64.42%

Late Dispatch: 312 holds

HELD ORDERS DELIVERED

81.49%

2,118 of 2,599 held orders

HELD ORDERS RETURNED

9.43%

245 of 2,599 held orders

TOP HOLD PATTERNS · WEEK 2

Riverside (H03)

Late Dispatch 312 holds

Action: review dispatch cut-off, route assignment, scan discipline and agent readiness before increasing permanent headcount.

Brookside (H05): three agents exceed the >15% return-ratio flag after >30 days tenure.

HIGH-RETURN AGENTS · Q5

A1045 · Belis Rowntree	**H05**	**26.93% returns**
94 returned / 349 assigned		
A1046 · Coris Halvorsen	**H05**	**21.98% returns**
91 returned / 414 assigned		
A1047 · Wenian Vantell	**H05**	**17.43% returns**
72 returned / 413 assigned		

The four-week forecast shows a five-agent gross shortfall.

Q7 uses each hub's 14-day attempts-per-order ratio and 34 planned attempts per agent per day.

PEAK STAFFING NEED BY HUB · BEFORE INTERVENTIONS

Hub	Active now	Peak required	Gross gap
H01 Greenfield	10	12	+2
H02 Lakeview	11	8	-3
H03 Riverside	12	13	+1
H04 Hillcrest	9	11	+2
H05 Brookside	11	10	-1
H06 Westwood	9	9	0

Gross positive gap: 5 agents (H01 +2, H03 +1, H04 +2). H02 and H05 have surplus capacity; only H02 can support H01 because transfers must stay inside a cluster.

DEPLOYMENT LOGIC

H01	**+2**	Same-cluster transfer from H02
H02	**-3 to -4**	Donor; 9 agents remain after moves
H03	**+1**	Programme reduces attempts; temporary target exception
H04	**+2**	Hire 2 Fixed agents
H05	**-1 to -2**	Surplus; no cross-cluster move
H06	**0**	No change

Approve a targeted plan hub by hub.

Two Fixed hires address the lasting gap at Hillcrest; transfers solve Greenfield; Riverside gets a process intervention.

HUB ACTIONS AND INCREMENTAL FIRST-MONTH COST

Hub	Action	First-month cost
H01 Greenfield	Receive 2 Fixed transfers from H02	BDT 4,000
H02 Lakeview	Transfer A1018 and A1015; 9 agents remain	No new spend
H03 Riverside	Launch hold-reduction programme; no immediate hire	BDT 15,000
H04 Hillcrest	Hire 2 Fixed agents; 11 agents total	BDT 43,800
H05 Brookside	No hire; review 3 high-return agents	No new spend
H06 Westwood	No staffing change	No new spend

Transfer candidates: A1018 (92.78% deliveries, 3.09% returns) and A1015 (90.86% deliveries, 2.65% returns). Both are Fixed agents in Cluster A.

The BDT 70,000 budget is sufficient.

The recommended response costs BDT 62,800 in the first month and retains a BDT 7,200 reserve.


BUDGET AVAILABLE
70,000
BDT

FIRST-MONTH SPEND
62,800
89.7% of budget

RESERVE
7,200
10.3% held back

PROGRAMME NET BENEFIT
10,682
Avoided hold fees less programme cost

BUDGET ALLOCATION

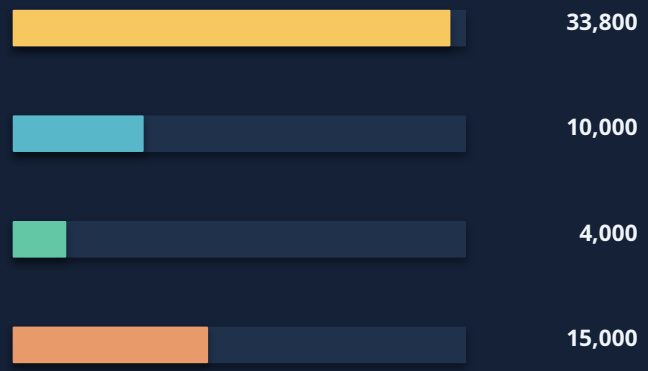

RIVERSIDE HOLD PROGRAMME · MODELLED

856 agent-side holds avoided over 4 weeks

25,682 BDT gross avoided hold charges

Assumption: a linear ramp to 50% reduction over 14 days from 27 Oct. Estimated net direct benefit after the BDT 15,000 programme fee: BDT 10,682.

Control the first 14 days; then reassess.

The plan is conditional. Use daily operating signals—not a fixed hiring promise—to release the reserve.

EARLY-WARNING TRIGGERS

Riverside agent-side holds	Track holds/order vs 25.71% Week 2 proxy. If no visible improvement by Day 14, revise intervention.
Riverside workload	Forecast 35.2 and 34.4 attempts/agent/day in Weeks 1-2. Escalate above 40 or if backlog rises.
H04 ramp	New hires plan at 24 attempts/day for first 7 days, then 34. Escalate if materially below ramp.
H02 donor buffer	After two transfers, 9 remain versus peak need of 8. No third transfer.
Demand / attempt intensity	Investigate if actual orders exceed forecast by 10% or attempts/order rises 5% above model.

DECISION REQUEST

Approve the BDT 62,800 plan.

1. Authorise two H02 -> H01 transfers.
2. Approve two Fixed hires at H04.
3. Release BDT 15,000 for H03 programme.

Retain BDT 7,200 reserve. Review results at Day 7 and Day 14; trigger new capacity only if the workload or backlog threshold is breached.

Dashboard source is prepared in Streamlit. Public hosting and the final shareable URL still need to be completed by the candidate.
